

Job Address: 8020 Hwy 3B , Trail, BC

Page 1 of 1



Photo 1: Headworks Pre-eng building



Photo 2: MBBR Southern Walls Poured

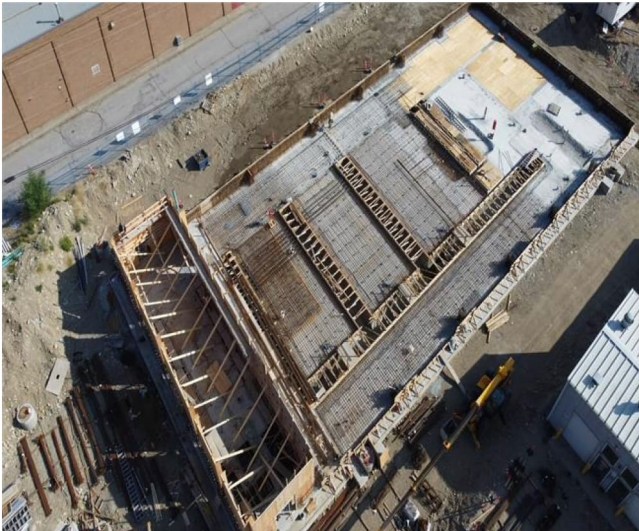


Photo 3: DAF Building SOG Rebar and Electrical Room Walls



Photo 4: Outfall Pipe Bolted Up

Project Facts:

Contractual Substantial Date:	2027-06-18
Projected Substantial Performance:	2027-09-07
Current Contract Value:	\$68,659,768.49

Project Description:

The project consists of the construction of the upgrades to the Regional District of Kootenay Boundary (RDKB) Columbia Pollution Control Centre, a wastewater treatment plant which includes a new headworks building c/w screens, grit removal system, new biological treatment tanks, Moving Bed Bio Reactor (MBBR) tanks, dissolved air flotation (DAF) clarifiers in a new DAF Process Building which also houses the UV disinfection system, the DAF polymer system, the reclaimed water system, heat recovery system, the plant electrical room & odour control systems for the Headworks.

Project Team:

Project Manager	Mason Van Vliet, Stuart Sanday
Project Coordinator	Amanda Samaddar, Vishal Jangra
Site Superintendent	Colby Darbyshire, Ron Devuyst

Site Brief:

- **Headworks:**
 - Masonry brick complete
 - Pre-eng structural steel framing complete. Cladding ongoing
 - Process mechanical scope to start next month
- **MBBR:**
 - GL 5, 6 walls and adjoining sections of GL I, H, G and F1 walls poured
 - Splitter box patching ongoing. Blower room walls being formed
- **DAF:**
 - Strip footings complete. Rebar for slab on grade and pony walls ongoing.
 - Slab on grade scheduled to be complete by end of September
 - Electrical Room walls formed and rebar ongoing
- **Yard Works:**
 - NPW Line MBBR to DAF
- **Outfall Pipe:**
 - Outfall pipe assembled. Effluent bypass operable
 - Barge being built for outfall install
 - Existing outfall to be removed in October
